

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float	2003												2004											
										J	A	S	O	N	D	F	M	A	M	J	J	A	S	O	N	D							
98	Interior Metal Studs	0	0	0	06AUG03*		12AUG03		4																								
94	Exterior Brick Veneer	19	19	0	06AUG03	01SEP03	15SEP03	09OCT03	28																								
105	Roofing/Flashing & Sheetmetal	17	17	0	06AUG03	28AUG03	23DEC03	14JAN04	99																								
1-10-116	DWV & Domestic Piping Rough	10	10	0	07AUG03	20AUG03	04DEC03	17DEC03	85																								
1-10-95	Interior Metal Studs	22	22	0	15AUG03	15SEP03	12AUG03	10SEP03	-3																								
1-10-117	HVAC Piping Rough In	15	15	0	21AUG03	10SEP03	18DEC03	07JAN04	85																								
1-10-124	Rough In Electrical Conduit	22	22	0	22AUG03	22SEP03	19AUG03	17SEP03	-3																								
102	Install Curtainwall (Rev'd	5	5	0	01SEP03	05SEP03	09OCT03	15OCT03	28																								
103	Install Aluminum Windows	2	2	0	01SEP03	02SEP03	14OCT03	15OCT03	31																								
1-10-118	Test Ductwork & Piping	5	5	0	11SEP03	17SEP03	08JAN04	14JAN04	85																								
107	Sprinkler Rough 1st Floor	16	16	0	17SEP03	08OCT03	17OCT03	07NOV03	22																								
1-10-119	Ductwork Insulation	10	10	0	18SEP03	01OCT03	15JAN04	28JAN04	85																								
1-10-99	Hang & Tape Drywall Finish	20	20	0	23SEP03	20OCT03	18SEP03	15OCT03	-3																								
110	Set Elevator Platform	20	20	0	01OCT03*	28OCT03	06JUL04	02AUG04	200																								
108	Sprinkler Rough 2nd Floor	16	16	0	08OCT03	29OCT03	07NOV03	28NOV03	22																								
109	Sprinkler Stand Pipe	4	4	0	29OCT03	03NOV03	28NOV03	03DEC03	22																								
12-31-152	Painting	30	30	0	04NOV03	15DEC03	04DEC03	14JAN04	22																								
12-31-153	Install Technology	10	10	0	16DEC03	29DEC03	15JAN04	28JAN04	22																								
12-31-154	Acoustical Ceiling	30	30	0	30DEC03	09FEB04	29JAN04	10MAR04	22																								
12-31-156	Flooring First Floor	25	25	0	10FEB04	15MAR04	11MAR04	14APR04	22																								
12-31-129	Install GRDs	10	10	0	10FEB04	23FEB04	20MAY04	02JUN04	72																								
12-31-157	Flooring Second Floor	15	15	0	16MAR04	05APR04	15APR04	05MAY04	22																								
12-31-149	Casework & Lockers	20	20	0	06APR04	03MAY04	06MAY04	02JUN04	22																								
12-31-158	Install Casework	10	10	0	06APR04	19APR04	06MAY04	19MAY04	22																								
Building C - Classrooms																																	
116	Footers & Piers	10	0	100	09JAN03A	15APR03A	09JAN03A	15APR03A																									
120	Underslab Utilities	10	0	100	09JAN03A	03APR03A	09JAN03A	03APR03A																									
117	Pedestals	3	0	100	21JAN03A	15APR03A	21JAN03A	15APR03A																									
118	Block Wall Below Grade	5	0	100	23JAN03A	15APR03A	23JAN03A	15APR03A																									
122	Slab on Grade	10	0	100	19MAY03A	02JUN03A	19MAY03A	02JUN03A																									
126	Erect Steel & Metal Deck	11	5	55	12JUN03A	23JUL03	12JUN03A	20JUN03	-23																								
2-7-176	Install Ductwork & VAVs	20	18	10	27JUN03A	01SEP03	27JUN03A	04FEB04	112																								
134	Exterior Metal Stud & Sheath	16	16	0	30JUN03A	28AUG03	30JUN03A	09SEP03	8																								
121	Underslab Stone/Insulation	1	0	100	30JUN03A	30JUN03A	30JUN03A	30JUN03A																									
119	Backfill Foundations	2	2	0	30JUN03	01JUL03	12JUN03	13JUN03	-12																								
124	Slab on Metal Deck	11	11	0	23JUL03	06AUG03	04AUG03	18AUG03	8																								
129	Set Masonry Door Frames	4	4	0	23JUL03	28JUL03	07AUG03	12AUG03	11																								
138	Set Roof Drains & Curbs	5	5	0	23JUL03*	29JUL03	19JAN04	23JAN04	128																								
123	Set Fire Dampers & Sleeves	3	3	0	23JUL03	25JUL03	03FEB04	05FEB04	139																								

Start Date

Finish Date

Data Date

Run Date

18NOV02

02SEP04

30JUN03

20FEB08 11:33

Early Bar

Float Bar

Progress Bar

Critical Activity

RL11

Input as of 6/30/03


EDiS 18 Nov 2002 Schedule

with Total Float Bar Shown

Sheet 2 of 7

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

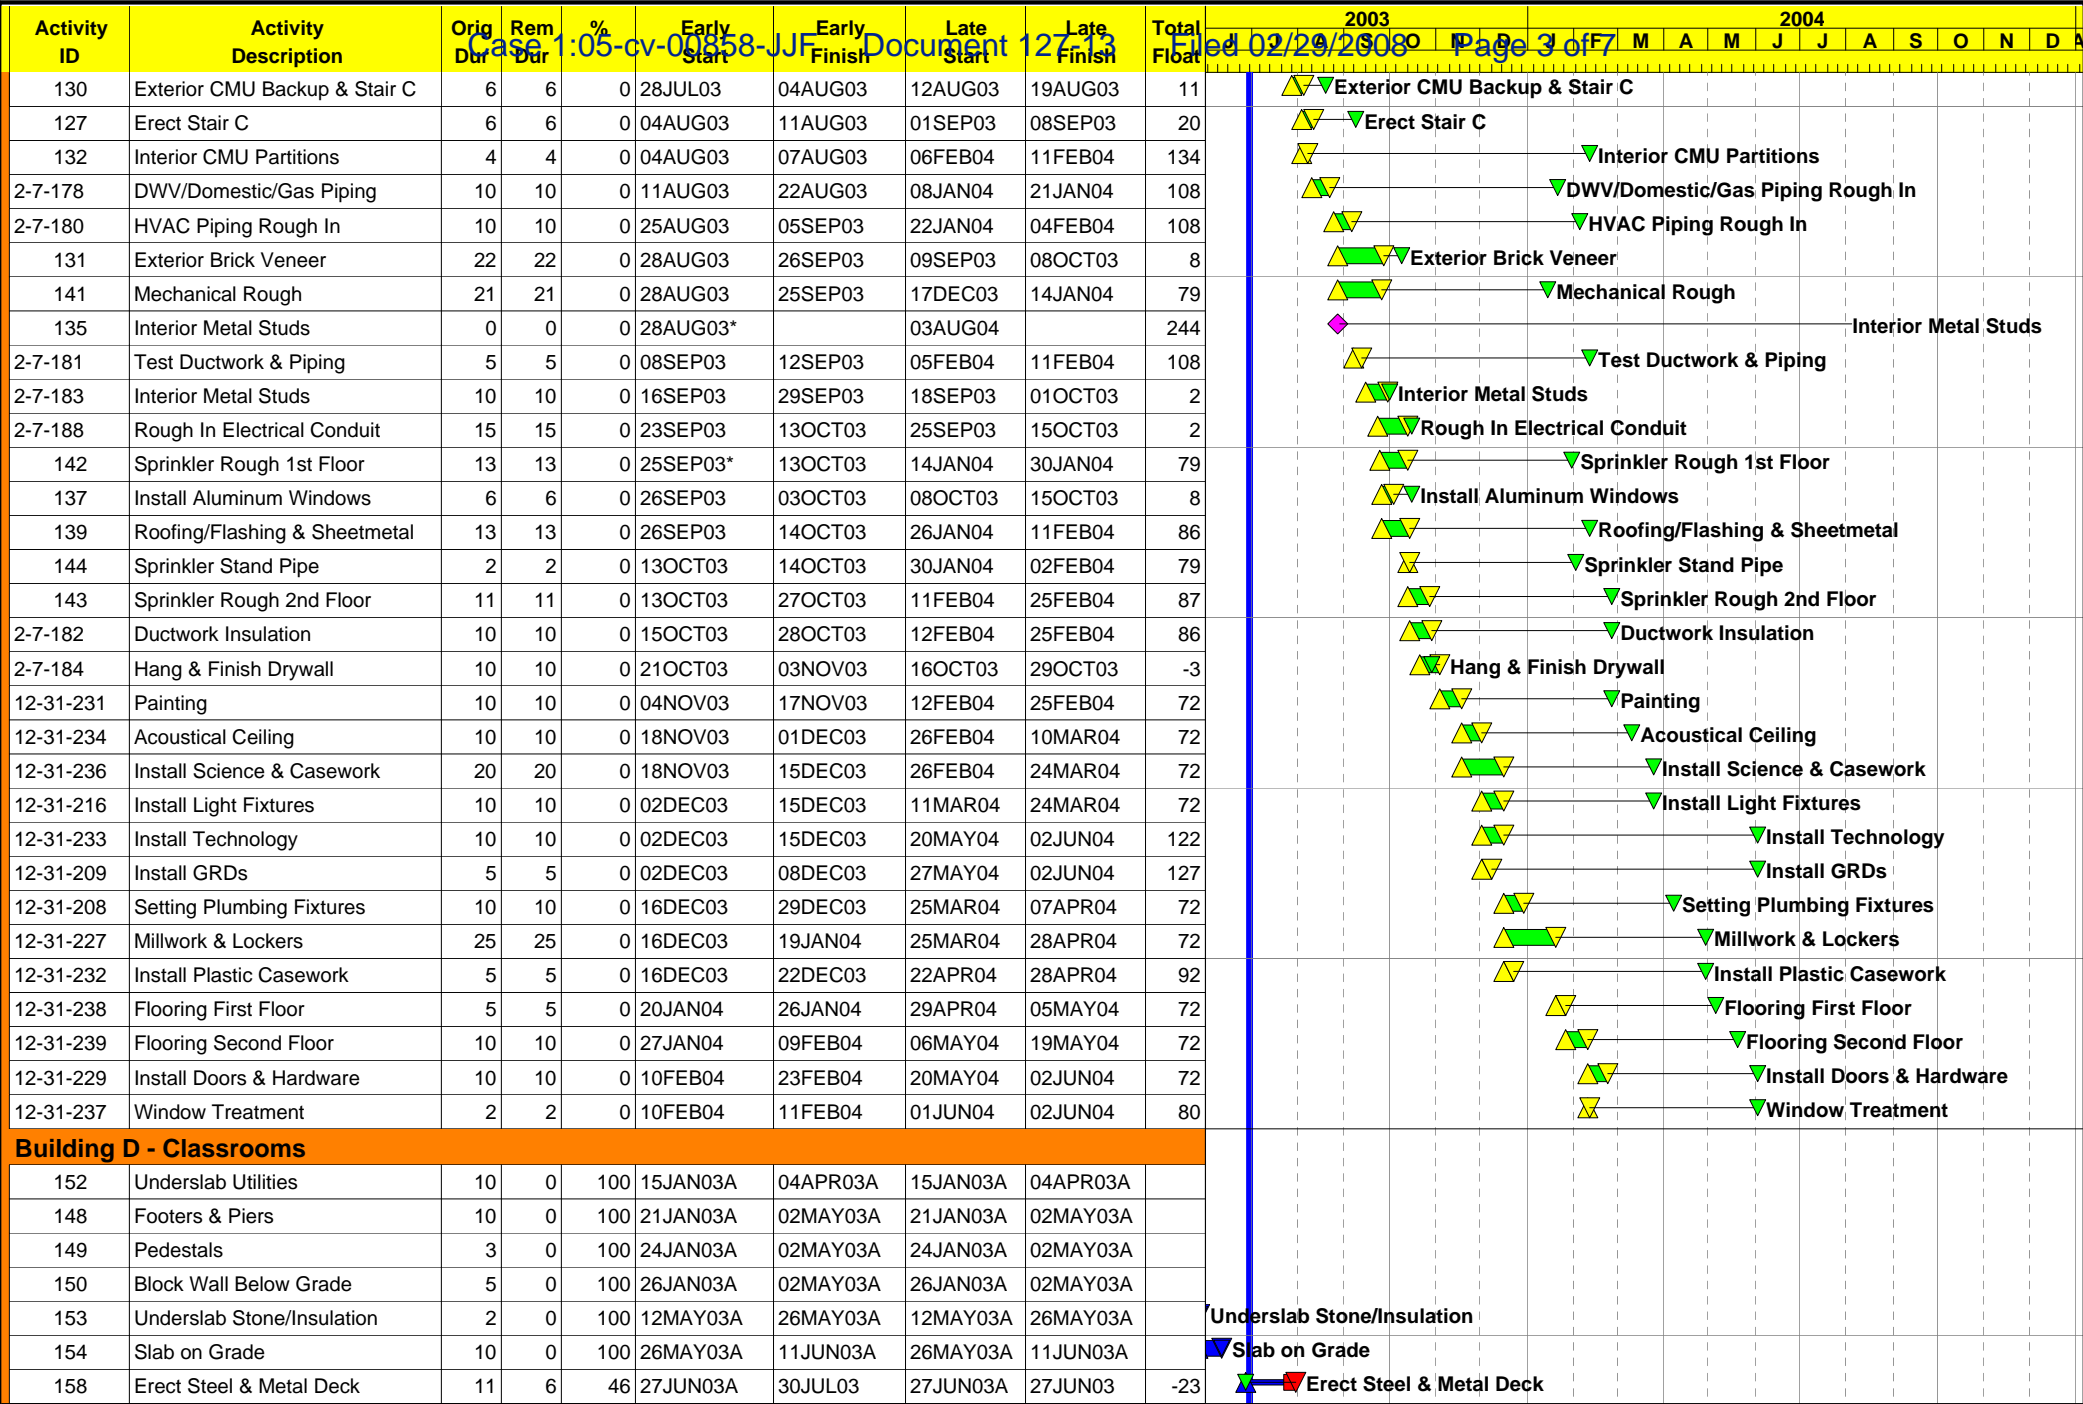

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float	2003												2004											
										F	M	A	M	J	J	A	S	O	N	D	A	F	M	A	M	J	J	A	S	O	N	D	A
151	Backfill Foundations	2	2	0	30JUN03	01JUL03	18JUN03	19JUN03	-8	Backfill Foundations																							
156	Slab on Metal Deck	11	11	0	30JUL03	13AUG03	10SEP03	24SEP03	30	Slab on Metal Deck																							
166	Exterior Metal Stud & Sheath	16	16	0	30JUL03	20AUG03	10SEP03	01OCT03	30	Exterior Metal Stud & Sheath																							
155	Set Fire Dampers & Sleeves	3	3	0	30JUL03	01AUG03	10OCT03	14OCT03	52	Set Fire Dampers & Sleeves																							
161	Set Masonry Door Frames	4	4	0	30JUL03	04AUG03	06FEB04	11FEB04	137	Set Masonry Door Frames																							
2-7-237	Install Ductwork & VAVs	20	20	0	30JUL03	26AUG03	25FEB04	23MAR04	150	Install Ductwork & VAVs																							
170	Set Roof Drains & Curbs	6	6	0	30JUL03	06AUG03	26FEB04	04MAR04	151	Set Roof Drains & Curbs																							
2-7-239	DWV/Domestic/Gas Rough In	10	10	0	01AUG03	14AUG03	11FEB04	24FEB04	138	DWV/Domestic/Gas Rough In																							
162	Exterior CMU Backup& Stair D	6	6	0	04AUG03	11AUG03	11FEB04	18FEB04	137	Exterior CMU Backup& Stair D 107																							
171	Roofing/Flashing & Sheetmetal	13	13	0	07AUG03*	25AUG03	05MAR04	23MAR04	151	Roofing/Flashing & Sheetmetal																							
164	Interior CMU Partitions	10	10	0	11AUG03	22AUG03	18FEB04	02MAR04	137	Interior CMU Partitions																							
2-7-240	HVAC Piping Rough In	15	15	0	15AUG03	04SEP03	25FEB04	16MAR04	138	HVAC Piping Rough In																							
163	Exterior Brick Veneer	16	16	0	20AUG03	10SEP03	15OCT03	05NOV03	40	Exterior Brick Veneer																							
173	Mechanical Rough	21	21	0	20AUG03	17SEP03	05JAN04	02FEB04	98	Mechanical Rough																							
167	Interior Metal Studs	0	0	0	20AUG03*		03AUG04		250	Interior Metal Studs																							
2-7-241	Test Ductwork & Piping	5	5	0	05SEP03	11SEP03	17MAR04	23MAR04	138	Test Ductwork & Piping																							
169	Install Aluminum Windows	6	6	0	10SEP03	17SEP03	05NOV03	12NOV03	40	Install Aluminum Windows																							
2-7-242	Ductwork Insulation	10	10	0	12SEP03	25SEP03	24MAR04	06APR04	138	Ductwork Insulation																							
2-7-223	Interior Metal Studs	10	10	0	30SEP03	13OCT03	02OCT03	15OCT03	2	Interior Metal Studs																							
2-7-248	Rough In Electrical Conduit	15	15	0	07OCT03	27OCT03	09OCT03	29OCT03	2	Rough In Electrical Conduit																							
174	Sprinkler Rough 1st Floor	11	11	0	14OCT03	28OCT03	02FEB04	16FEB04	79	Sprinkler Rough 1st Floor																							
175	Sprinkler Rough 2nd Floor	11	11	0	28OCT03	11NOV03	16FEB04	01MAR04	79	Sprinkler Rough 2nd Floor																							
2-7-224	Hang & Finish Drywall	10	10	0	04NOV03	17NOV03	30OCT03	12NOV03	-3	Hang & Finish Drywall																							
176	Sprinkler Stand Pipe	2	2	0	11NOV03	12NOV03	01MAR04	02MAR04	79	Sprinkler Stand Pipe																							
12-31-313	Painting	15	15	0	18NOV03	08DEC03	03MAR04	23MAR04	76	Painting																							
12-31-314	Install Technology	10	10	0	09DEC03	22DEC03	24MAR04	06APR04	76	Install Technology																							
12-31-308	Millwork & Lockers	25	25	0	09DEC03	12JAN04	29APR04	02JUN04	102	Millwork & Lockers																							
12-31-315	Acoustical Ceiling	15	15	0	23DEC03	12JAN04	07APR04	27APR04	76	Acoustical Ceiling																							
12-31-290	Setting Plumbing Fixtures	10	10	0	30DEC03	12JAN04	08APR04	21APR04	72	Setting Plumbing Fixtures																							
12-31-316	Install Projection Screen	2	2	0	13JAN04	14JAN04	28APR04	29APR04	76	Install Projection Screen																							
12-31-288	Install Light Fixtures	5	5	0	13JAN04	19JAN04	27MAY04	02JUN04	97	Install Light Fixtures																							
12-31-291	Install GRDs	5	5	0	13JAN04	19JAN04	27MAY04	02JUN04	97	Install GRDs																							
12-31-317	Install Window Treatments	2	2	0	15JAN04	16JAN04	30APR04	03MAY04	76	Install Window Treatments																							
12-31-318	Flooring First Floor	10	10	0	19JAN04	30JAN04	04MAY04	17MAY04	76	Flooring First Floor																							
12-31-319	Flooring Second Floor	7	7	0	02FEB04	10FEB04	18MAY04	26MAY04	76	Flooring Second Floor																							
12-31-311	Install Doors & Hardware	10	10	0	02FEB04	13FEB04	20MAY04	02JUN04	78	Install Doors & Hardware																							
12-31-320	Install Casework	5	5	0	11FEB04	17FEB04	27MAY04	02JUN04	76	Install Casework																							
Building E - Classrooms																																	
181	Pedestals	3	0	100	02FEB03A	15APR03A	02FEB03A	15APR03A																									

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float	2003												2004																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
										J	F	M	A	M	J	J	A	S	O	N	D	A	M	J	J	A	S	O	N	D	A																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
12-31-440	Install Light Fixtures	10	10	0	23MAR04	05APR04	20MAY04	02JUN04	42																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	

Start Date

Finish Date

Data Date

Run Date

18NOV02

02SEP04

30JUN03

20FEB08 11:33

Early Bar

Float Bar

Progress Bar

Critical Activity

RL11

Input as of 6/30/03

EDiS 18 Nov 2002 Schedule

with Total Float Bar Shown

Sheet 7 of 7

Date	Revision	Checked	Approved

© Primavera Systems, Inc.

Final Punchlist & Move In

Substantial Completion
